



Notice of Project
Western University
Facilities Management
Client Services 519-661-3304 (fmhelp@uwo.ca)

Submit by E-mail

Print Form

Project Number: 9C6542	<input checked="" type="checkbox"/> Miniature Attached	Date/Schedule: Thursday, August 6, 2015
Project Name: CG Way Finding & Signage		Time: TBD

Building(s) Affected: #1 WELDON LIBRARY (WL)	#2 UNIVERSITY COMMUNITY CENTRE (UCC)
#3	#4

Areas/Rooms Affected, Alternate Route/Service:

WL Exit 2 and Exit 3; it is not anticipated that access to Exit 1 will be restricted in any manner.

Service to be interrupted: #1 Corridor	#2
#3	#4

Description/Reason for Project:

Glass Canada sub contracted to Fast Signs will be on site; concrete beach and the area of WL entrance with the necessary equipment and barricades to remove the 2 glass panels from the WL building signs. One sign located on the east wall adjacent to Exit 2, and the second sign on the west face of the building stairwell structure, above Exit 3 (in the vicinity of Exit 1).

Project Manager/ Co-ordinator: Greg Ackland	Phone # 519-661-2111 x80324	Cell # 519-521-0713
Signature/ Stamp: 	Client Contact:	Phone #
	Designer Consultant:	

Contractor: Glass Canada sub contracted to Fast Signs	Cell # 519-495-2822
---	---------------------

Emergency Phone List: (to CCPS Only) ☐ Attached ☐ To Follow

Special Conditions (Noise, Odors, Asbestos, Etc.)

☐ Asbestos ☐ Type 3 ☐ Type 2 ☐ Type 1 ☐ Contractor ☐ In House Team ☐ Other
☐ Information Sheet Sent To Client


Comments:

Shutdowns/Interruptions(Approximate Schedule):

Electrical Power <input type="checkbox"/>	Date: _____	Elevators <input type="checkbox"/>	Date: _____	ITS <input type="checkbox"/>	Date: _____
Domestic Water <input type="checkbox"/>	Date: _____	Fire Alarms <input type="checkbox"/>	Date: _____	Other <input type="checkbox"/>	Date: _____
Steam <input type="checkbox"/>	Date: _____	Chilled Water <input type="checkbox"/>	Date: _____		
Hot Water Heating <input type="checkbox"/>	Date: _____	Roads / Lots <input type="checkbox"/>	Date: _____		

Issued By: APPROVED	Date: _____
Signature/ Stamp: <i>By Dan Trudgeon at 11:01 am, Jul 30, 2015</i>	Date: _____


Note:

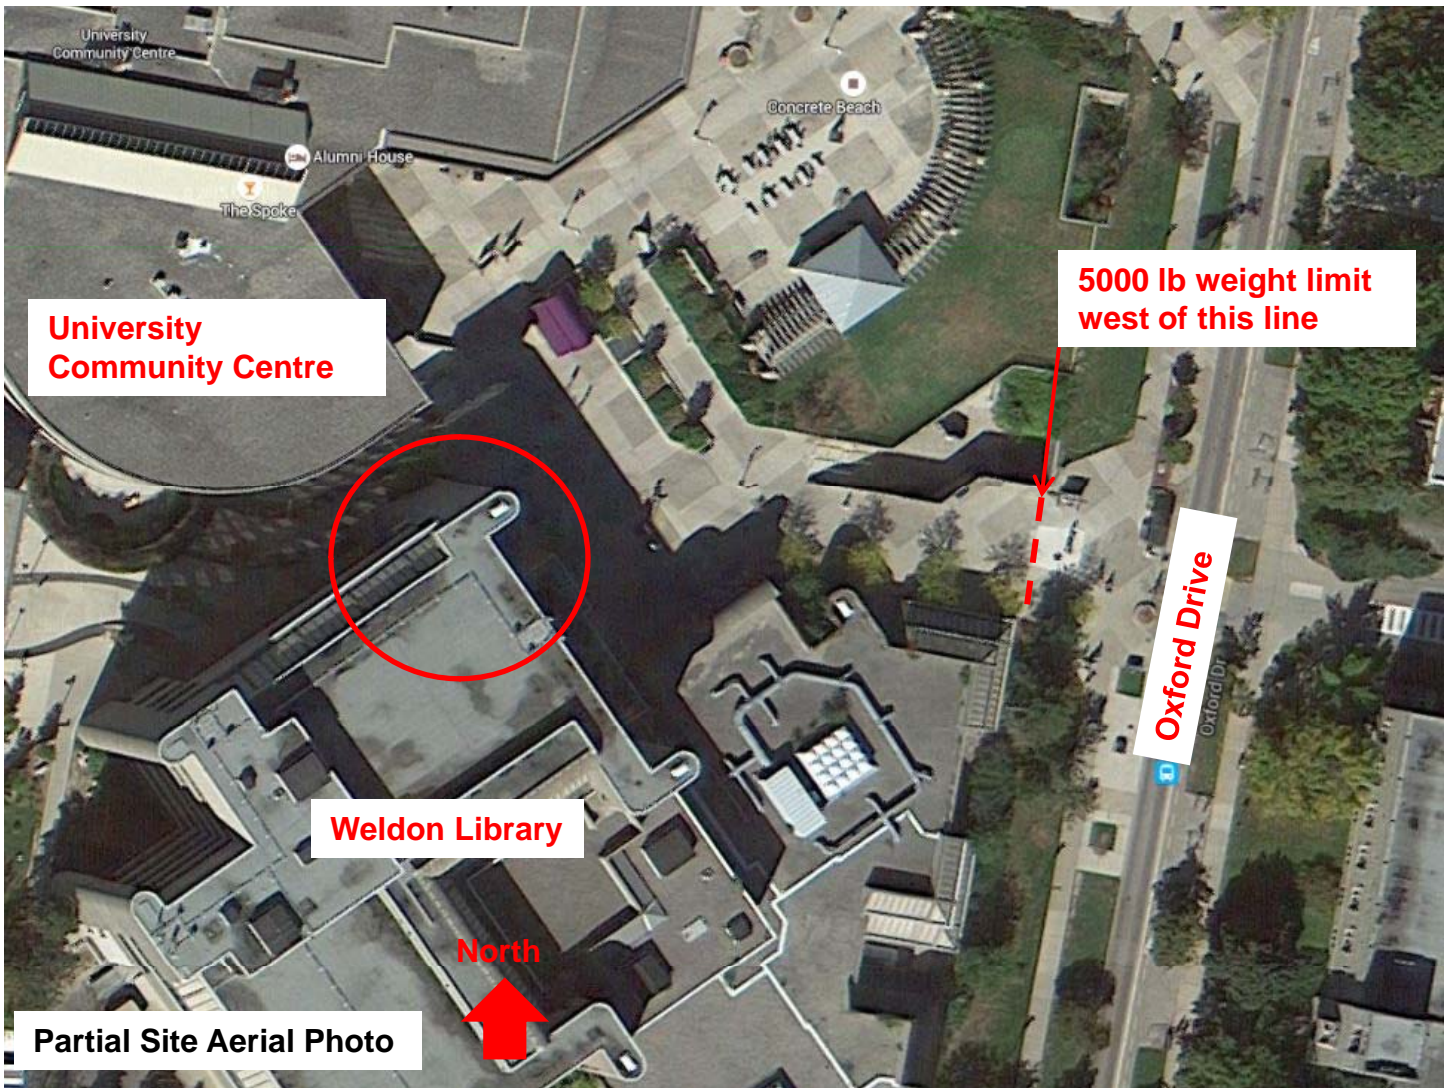

Limited access to signs for the work due to stairs and load limit on the access to and in the area of the work.

Weldon Library Exterior Sign Panel Replacements



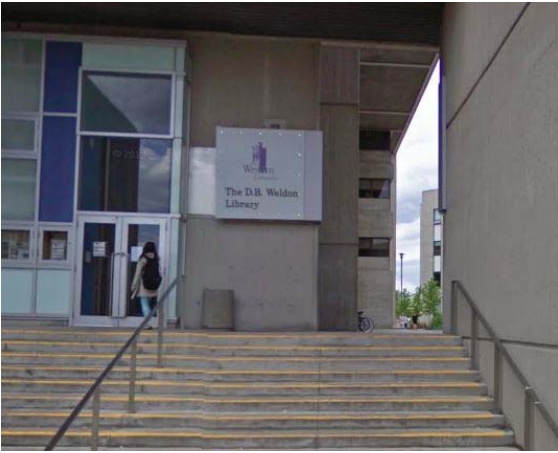

East Sign



existing hinged side panel




- remove the existing 72"x72"x1/4"-3/8" thick glass sign face panel; including through glass mounting hardware as required; remove applied letters & turn over to Western; destroy and dispose the glass panel,
- clean out sign box; replace fluorescent lighting, ballasts, and related electrical apparatus; retain electrical service 15A, 120V for reuse,
- complete new LED lighting as required to maintain similar light level as existing; maintain existing service & photocell control,
- supply and install a new retrofitted 4 sided aluminum frame (approx. 66 1/2" wide x 66" high) finished to match existing sign box hinged to a side with restraint or top of the existing sign box frame; details of the existing sign and sign box construction are not on file / available; complete site review as necessary to establish scope,
- supply and install a new acrylic sign face complete with white background, Western Crest and "The D.B. Weldon Library" as per the layout attached,

SK2

Weldon Library Exterior Sign Panel Replacements

R0 – 2015-06-22

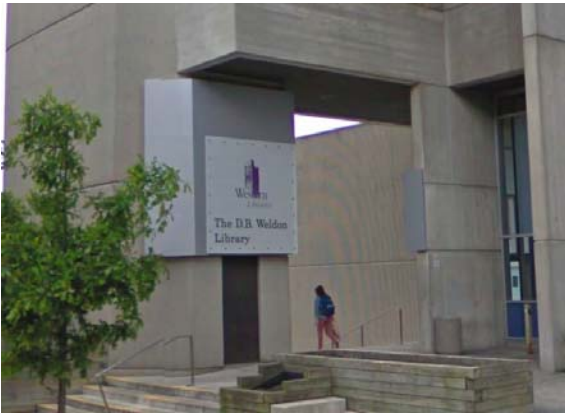

West Sign



- remove the existing 96"x96"x1/4"-3/8" thick glass sign face panel; including through glass mounting hardware as required; remove applied letters & turn over to Western; destroy and dispose the glass panel,
- clean out sign box; replace fluorescent lighting, ballasts, and related electrical apparatus; retain electrical service 15A, 120V for reuse,
- complete new LED lighting as required to maintain similar light level as existing; maintain existing service & photocell control
- supply and install a new retrofitted 4 sided aluminum frame (approx. 91" wide x 90" high) finished to match existing sign box, hinged to a side with restraint or top of the existing sign box frame; details of the existing sign and sign box construction are not on file / available ; complete site review as necessary to establish scope,
- supply and install a new acrylic sign face complete with Western Crest and "The D.B. Weldon Library" as per the layout attached



← existing hinged side panel

Weldon Library Exterior Sign Panel Replacements

SK3

R0 – 2015-06-22



The D.B. Weldon Library

Proposed sign panel layout; typical for both signs; graphic file, font, crest image file, etc. will be provided.
